


## **Sixth Street Water Main Replaced; Site Utility Work Continues and Will Extend to Fifth Street**

As the excavation and foundation phase of our project continues, site utility work is also ongoing..

On Wednesday, May 31<sup>st</sup>, replacement of the water main at Sixth Street was completed.

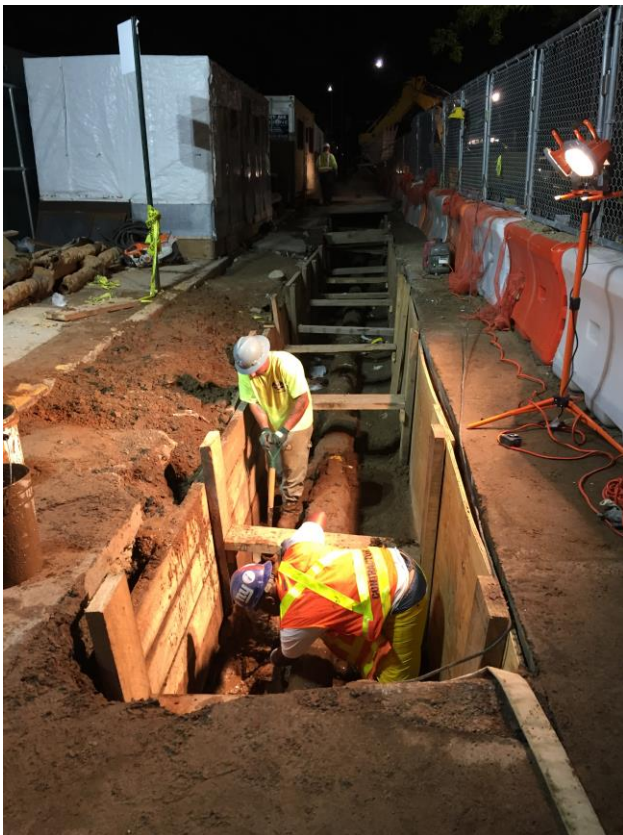

**Replacement of the water main on Sixth Street.**

Other Sixth Street site utility work is continuing and is also scheduled to begin on Fifth Street. Intermittent sidewalk and parking closures will occur on both Fifth and Sixth Streets as this work is done.

Construction of the Con Edison vaults at Fifth Street will necessitate closing the south side of the sidewalk and parking lane for approximately 100 feet from the corner Eighth Avenue, for a period of about two months. Pedestrians will be redirected to the opposite side of the street during this time. The construction of the Con Edison vaults will require a limited amount of trucking (for the concrete operation) on Fifth Street.

In preparation for the next phase of construction: the steel phase, sidewalk bridging and protection will be installed around the perimeter of the construction site and at the “core properties” (the small buildings remaining on the south side of Fifth Street). This operation will be similar to that seen during the demolition phase of the project and will require intermittent sidewalk closures.

## Work Hours

Current construction work hours are Monday through Friday, from 7:00 a.m. until 6:00 p.m.

When there is a need to make up for delays due to weather or other unforeseen circumstances, work is done between 9 a.m. and 5 p.m. on *occasional Saturdays*, No trucking, concrete pours or other noisy work occurs on Saturdays.

Some equipment deliveries take place during off hours and notices of both Saturday work and early deliveries will continue to be sent in advance.

## Upcoming Work

### June 18th – June 24<sup>th</sup>

- Excavation and foundation work continues.
- Site utility work at Sixth Street continues.
- On-site underground utilities work begins.

### June 25th – July 1<sup>st</sup>

- Excavation and foundation work continues.
- Site utility work at Sixth Street continues.
- On-site underground utilities work continues.
- Fifth Street sidewalk and lane close for construction of Con Edison vaults.

### July 2nd – July 8th

*(Job closed on July 4)*

- Excavation and foundation work continues.
- Site utility work at Fifth Street begins.

- On site underground utilities work continues.
- ConEd vault construction begins.

### July 9th – July 15th

- Excavation and foundation work continues.
- Site utility work at Fifth Street continues.
- ConEd vault construction continues.
- Sidewalk bridge and protection installation begins.

## For More Information...

This newsletter and previous issues are available at [nyp.org/Brooklyn](http://nyp.org/Brooklyn). Click on the "Center for Community Health Construction Update" tile. Interested members of the community can also request that the newsletter be sent directly to their email addresses by making this request to Lyn Hill at [lyh9001@nyp.org](mailto:lyh9001@nyp.org).

In addition, a number of relevant documents, including the Building Monitoring Plan submitted to and accepted by the Landmarks Preservation Commission, can be accessed at: <https://projects.lendlease.com/PrologConverge/WebClient/navigate.aspx?projguid=46778806-5e94-4f44-beb9-8e404a4bb6cf&Req=folder&no msg=1&Key=26344>.

**User name: Community Task Force**

**Password: CTF11215**

Questions/concerns about the project may be addressed to:

Lyn S. Hill, Vice President for Communication and External Affairs  
at [lyh9001@nyp.org](mailto:lyh9001@nyp.org) or (718) 780-3301.

Questions/concerns about the construction should be addressed to:

Sharon Stern, Community-Project PR Liaison  
at Lendlease, (212) 592-6826.
